



Arlington High School Building Project

AHS Construction Update – 3/4/2022

Arlington HS Construction Schedule: April 2020 – April 2025

Construction Details

Phase 1 construction is nearly complete. The Phase 1 wings will open on 2/28 and the new Auditorium is expected to open in early April. Phase 2 begins immediately, and work areas include the Collomb building and courtyard, the Link building and the Lowe Auditorium, which have been cleared out and closed off from the existing school. Work areas also include the softball field, baseball field and a portion of the East parking lot/rotary. Landscaping around Main Entrance #1 will take place in the spring.

COVID-19 Update

The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>


For more information, visit:
www.ahsbuilding.org

Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



PHASE 2 BUILDING CONSTRUCTION (February 2022 – September 2023)

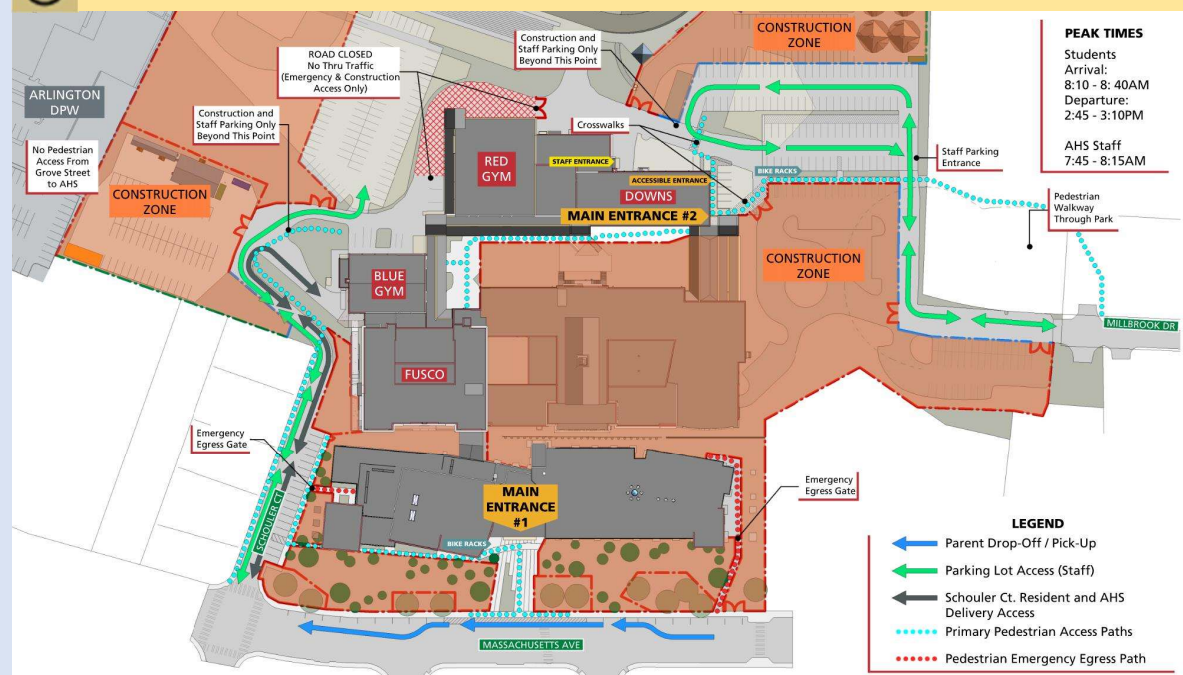

02-22-2022 DRAFT

Construction Look Ahead – Week of March 7, 2022

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts

- Permanent Main Entrance #1 open
- Millbrook Drive rotary offline
- Deliveries to project ongoing

General Site Activities:

- Phase 2 Enabling:
 - Courtyard enabling
 - Construction fence installation
 - Collomb building / Link building / Lowe Auditorium abatement
- Phase 1 Building Closeout:
 - Auditorium finishes
 - Punchlist and final testing
 - Exterior paving and lighting install
 - Start Phase 2 demolition prep
- West Parking Lot (adjacent to DPW):
 - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
 - Contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site

Weekend Work/Holiday Work:

- Saturday work is required for the foreseeable future
- Sunday work required on 3/6/22



Skanska USA Inc.
Owner's Project Manager



Consigli Construction Co., Inc.
Construction Manager at Risk



HMFH Architects, Inc.
Architect




ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF MARCH 7TH, 2022

Progress Photographs – Taken Week of 3/1/2022



Photograph 1: Discourse Lab

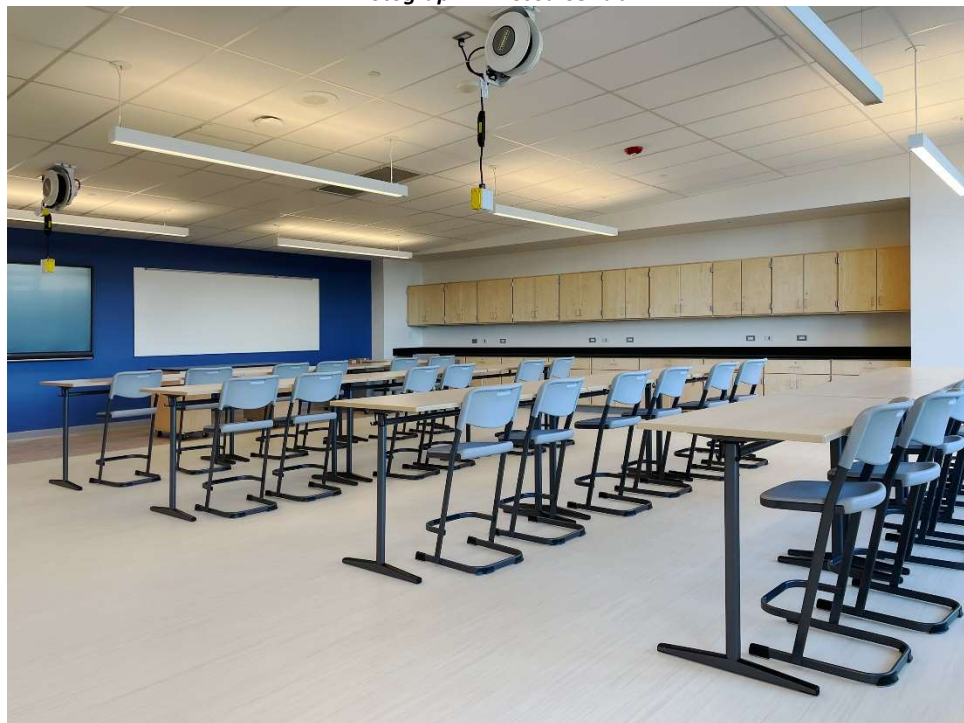

Photograph 2: Science Classroom



ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF MARCH 7TH, 2022



Photograph 3: Building D/E South Elevation (Main Entrance #1)



Photograph 4: Building D South Elevation (Mass Ave)



CONSIGLI
Est. 1905

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF MARCH 7TH, 2022



Photograph 5: Building D East Elevation



Photograph 6: Building E West Elevation (Schouler Court)
